


Renew Stations STATUS & MILESTONES

EXPENDED Thru 09/2023: **\$75.6**
 FORECAST Thru 06/2025: **\$107.1**
 TOTAL PROGRAM VALUE: **\$210**
 PERIOD CASHFLOW: **\$0.1**

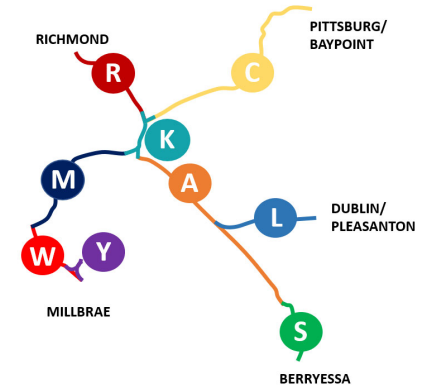

STATUS – Renew Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
0	1	0	4	3	8

MILESTONES			
Completed (Jul 2023 – Sep 2023)	Q2 (Oct 2023 – Dec 2023)	Q3 (Jan 2024 – Mar 2024)	Q4 (Apr 2024 – June 2024)
<ul style="list-style-type: none"> Completion of Construction for Platform Lighting for Powell St. Station Modernization Completion of Powell St. Station Platform Escalator P3, and Embarcadero Station Platform Escalator P2 for Market Street Escalators Project Begin Construction for Replacement of Embarcadero Station Platform Escalator P6, Montgomery St. Platform Escalator P3, and Powell St. Platform Escalator P1 for Market Street Escalators Project <i>Completed Construction of Canopy 3 at Embarcadero Station</i> 	<ul style="list-style-type: none"> <i>Completion of Construction for Canopy 11 at Montgomery Station and Canopy 15 at Powell Station</i> 	<ul style="list-style-type: none"> Completion of Civic Center Platform Escalator P1, and Montgomery St. Platform Escalator P3 for Market Street Escalators Project 	<ul style="list-style-type: none"> <i>Completion of Construction for Canopy 2 at Embarcadero Station, Canopy 9 at Montgomery Station, and Canopy 6 at Embarcadero Station</i>

Watchlist:

- Construction of Canopies

Italic: Modified milestones from previous report.

