


Station Access STATUS & MILESTONES

EXPENDED Thru 09/2023: \$40.6
 FORECAST Thru 06/2025: \$69.2
 TOTAL PROGRAM VALUE: \$135
 PERIOD CASHFLOW: \$0.9

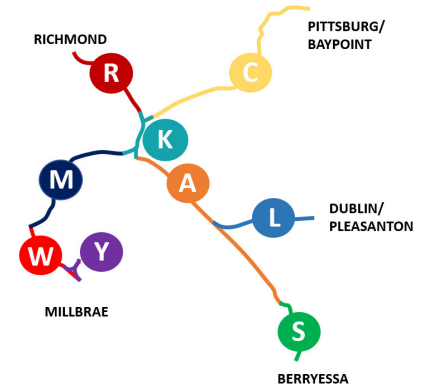

STATUS – Expand Safe Access to Stations

# Projects in Planning	# Projects in Design	# Projects in Bid/Award	# Projects in Construction	# Projects Completed	TOTAL # Projects
0	10	4	4	12	30

MILESTONES			
Completed (Jul 2023 – Sep 2023)	Q2 (Oct 2023 – Dec 2023)	Q3 (Jan 2024 – Mar 2024)	Q4 (Apr 2024 – June 2024)
<ul style="list-style-type: none"> • Completion of Construction for 12th St. Bike Racks • Completion of Design for the MacArthur Station Access Improvements • <i>Notice to Proceed for the Accessibility Improvement Program</i> • <i>Began Demolition for ADA Access Corrections at Fremont and Bay Fair Stations</i> 	<ul style="list-style-type: none"> • Begin Construction of SR2B-funded Walnut/Liberty Protected Intersection near Fremont Station • Completion of SR2B-funded Iron Horse Trail Bridge Project 	<ul style="list-style-type: none"> • Completion of Design for the Dublin/Pleasanton Access Improvement Project • Begin Construction of Ashby Access Improvement Project • <i>Begin Demolition for ADA Access Corrections at Hayward Station</i> 	<ul style="list-style-type: none"> • <i>Begin Demolition for ADA Access Corrections at Castro Valley Station</i> • <i>Completion of Design for New Bike Station (400 Bicycles)</i>

Watchlist:

- City of Pittsburg BART Ped/Bike Connectivity Project Construction
- Walnut Ave/Liberty Street Protected Intersection Project
- Iron Horse Trail Bridge at Dublin Blvd

Italic: Modified milestones from previous report.

BART Safety Reliability and Traffic Relief Program (Measure RR)
 January 2024

